




CONSULTANTS IN ENGINEERING,
ENVIRONMENTAL SCIENCE & PLANNING

APPENDIX 2

Site Walkover Checklist and Photographic Log

For inspection purposes only.
Consent of copyright owner required for any other use.

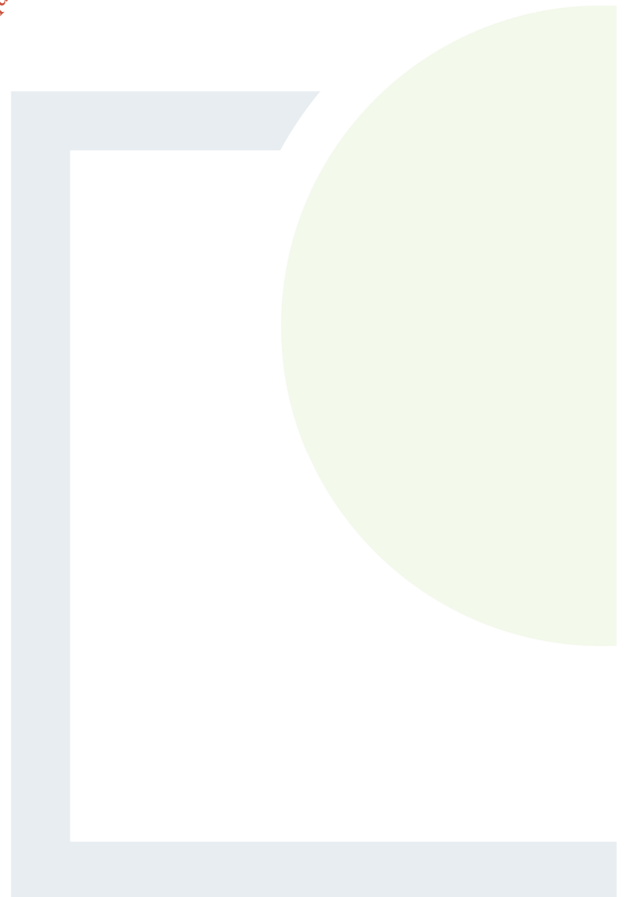

Appendix

Site Walkover Photographs

For inspection purposes only.
Consent of copyright owner required for any other use.



PHOTOGRAPHIC LOG



Client Name: Kerry
County Council

Site Location: Lenamore

Project Number: P1766

Photo No.

Date:

1

23/10/19

Description:

Access track to BH
location



For inspection purposes only.
Consent of copyright owner required for any other use.

Photo No.

Date:

2

23/10/19

Description:

BH01 located at the edge
of forestry



PHOTOGRAPHIC LOG



Client Name: Kerry
County Council

Site Location: Lenamore

Project Number: P1766

Photo No.

3

Date:

23/10/19

Description:

SW01 (upstream)



Photo No.

4

Date:

23/10/19

Description:

SW01 (downstream)



PHOTOGRAPHIC LOG



Client Name: Kerry
County Council

Site Location: Lenamore

Project Number: P1766

Photo No.

5

Date:

23/10/19

Description:

Forestry site



For inspection purposes only
Consent of copyright owner required for any other use

Walkover Survey Checklist

Historic Kerry Landfills - Lenamore

Walkover Survey Checklist		
Information	Checked	Comment (include distances from Site Boundary)
1. What is the current land use?	✓	Forestry and access road (wind turbines in close proximity)
2. What are the neighbouring land uses?	✓	Forestry, access road, bog (100m north)
3. What is the size of the site?	✓	Circa 0.75 ha
4. What is the topography?	✓	Relatively flat – slightly sloped (inclining to the west)
5. Are there potential receptors (if yes, give details)?	✓	Nearby residences, groundwater, surface water (River Gurteennacloona)
Houses		
Surface water features (if yes, distance and direction of flow)?	✓	Yes, River Gurteennacloona runs through the northern extent of the site, flowing in a north-west south-east direction
Any wetland or protected areas?	✓	Bogland 100m north of site
Public water supplies?	✓	Not identified
Private wells?	✓	Possible local usage
Services?	✓	None
Other buildings?	✓	None on-site
Other?	✓	No
6. Are there any potential sources of contamination (if yes, give details)?	✓	Buried waste
Surface waste (if yes, what type)?	✓	None noted
Surface ponding of leachate	✓	None present
Leachate seepage	✓	None noted
Landfill gas odours	✓	None noted
7. Are there any outfalls to surface water? (If yes, are there discharges and what is the nature of the discharge?)	✓	No evidence
8. Are there any signs of impact on the environment? (if yes, take photographic evidence)	✓	None noted.
Vegetation die off, bare ground	✓	None noted
Leachate seepages	✓	None noted
Odours	✓	None Noted
Litter	✓	None
Gas bubbling through water	✓	None noted
Signs of settlement	✓	No
Subsidence, water logged areas	✓	No evidence

Walkover Survey Checklist

Historic Kerry Landfills - Lenamore

Walkover Survey Checklist		
Information	Checked	Comment (include distances from Site Boundary)
Drainage or hydraulic issues	✓	None noted
Downstream water quality appears poorer than upstream water quality	✓	No
9. Are there any indications of remedial measures? (Provide details)	✓	No
Capping	✓	No waste evident
Landfill gas collection	✓	No
Leachate collection	✓	No
10. Describe fences and security features (if any)	✓	No fencing surrounding site
Any other relevant information?		

For inspection purposes only.
Consent of copyright owner required for any other use.
